

UNIVERSITY OF ARKANSAS DEPARTMENT OF ATHLETICS



**Donald W. Reynolds Razorback Stadium
North End Zone Addition and Stadium Renovation**

Project Update as of April 1, 2018

EXECUTIVE SUMMARY



The Donald W. Reynolds Razorback Stadium Project is on schedule and on budget. The project has been funded at \$160M through proceeds of a bond issue, capital commitments from new suites and loge boxes, and Athletic Department revenues.

The Athletic Department completed the \$120M bond issue in October 2016. This is the only bond issue for the project. Bond proceeds are being spent over a 2-year period, and will generate an additional \$800K in net investment earnings. The department saved over \$11M by issuing bonds in October 2016, before rates began rising; and saved over \$40M by amortizing bonds over 20 years as opposed to 30 years.

The Razorback Foundation has signed agreements for 6 Founder's Suites, 31 North End Zone Suites, and 67 North End Zone Loge Boxes. These agreements have generated gift commitments of \$41.1M. Commitments are being paid over periods up to seven years, with \$29.2M being received towards project funding, and \$11.9M being received over the next five years towards funding debt service.

The Athletic Department funded \$5M in FY16 and \$5M in FY17. The department began selling new North End Zone club seats in September, which will generate additional revenue for FY2019 and beyond towards funding debt service.

Due to the success in securing commitments for the new suites and loge boxes, and the overall solid financial position of the Athletic Department, Razorback Foundation reserves will not be used for the stadium project as originally planned.

PREMIUM SEATING COMMITMENTS



New Premium Seating Commitments

6	Founders Suites
16	North End Legends Suites
10	North End Victory Suites
6	North End Level Two Suites
67	North End Loge Boxes
1,280	North End Club Seats

CONSTRUCTION UPDATE



The stadium project remains on schedule for completion in advance of the first home football game on September 1, 2018.

Construction work in the north addition continues to progress well and on schedule. Current expansion work includes exterior limestone, glass window systems, precast concrete risers for the seating bowl, interior metal framing, MEP work, and steel stairs for access to the existing stadium. The contractor has met the scheduled timeline for power to the building, and is on schedule for conditioned air to the building in April.

Current existing stadium renovation work includes final ceilings and painting within the existing suites and lobby areas, new seating installation, club restroom finishes, and steelwork for the new Founders Suites.

The contractor is working through the final bid processes for stadium signage and furniture.

Live updates can be seen at <https://app.oxblue.com/open/universityofarkansas>

CONSTRUCTION UPDATE



CONSTRUCTION UPDATE



CONSTRUCTION UPDATE




43 - 11 North Elevation Masonry, Glazing and Metal Panel progress



44 - 11 NE Stair Tower

CONSTRUCTION UPDATE

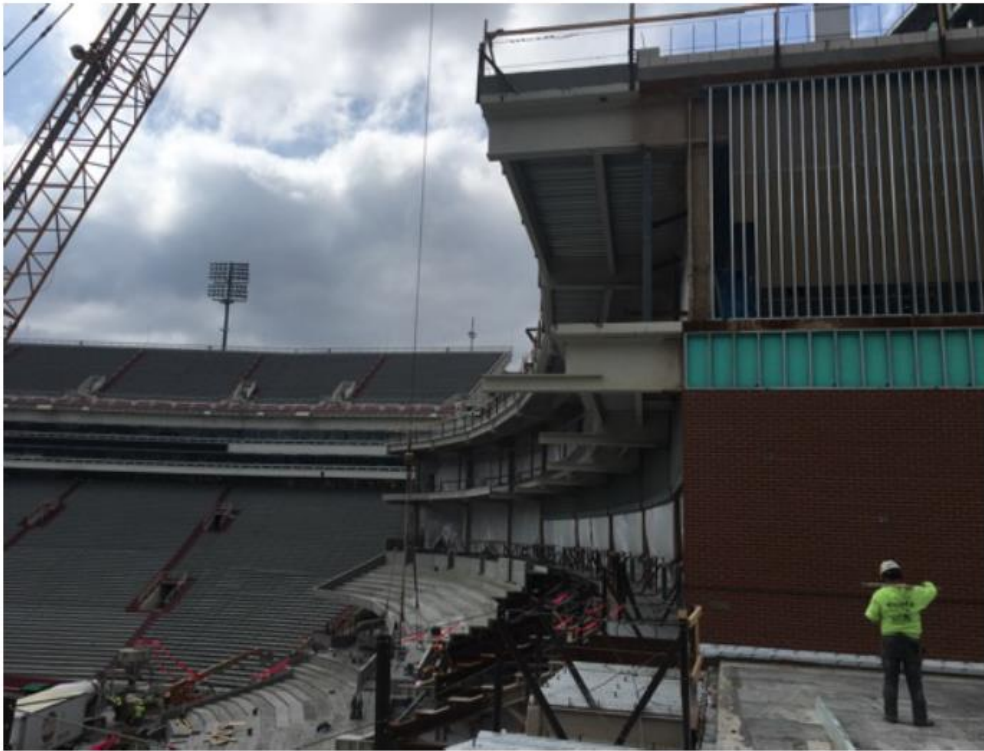

44 - 07 Precast installation progress from Level 03 looking West




43 - 06 Masonry & EFIS Progress at Level 02 Concourse

CONSTRUCTION UPDATE



43 - 03 Renovation Progress in West Lower Suites

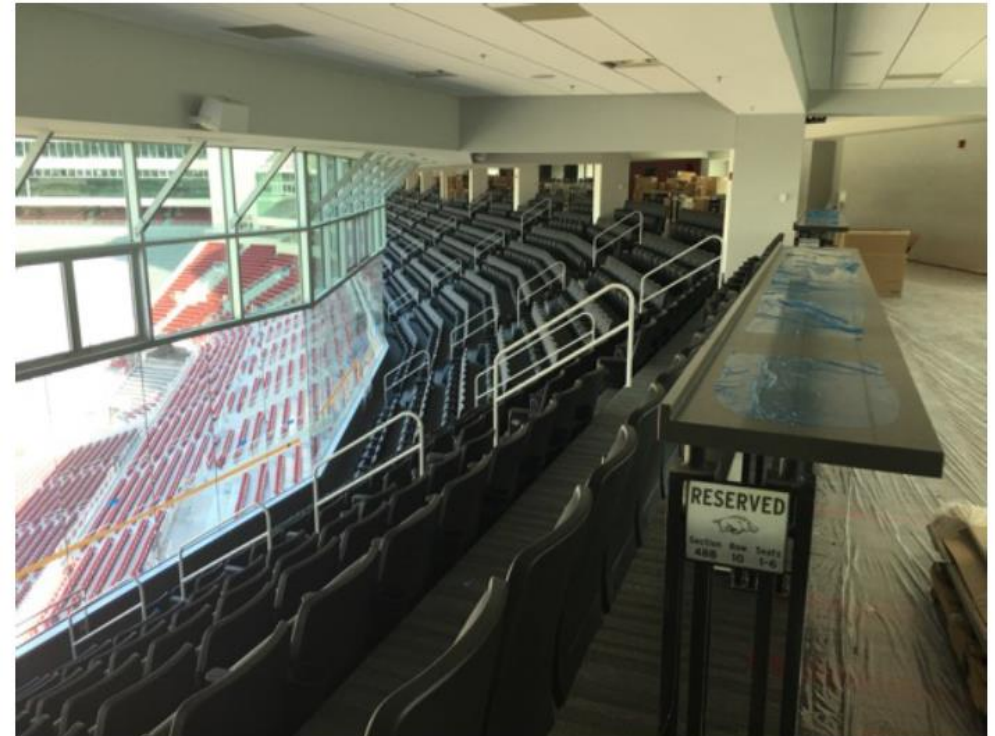

44 - 01 Renovation process in South Upper Club

PROJECT BUDGET UPDATE



The stadium project budget remains at \$160M. Through March 2018, \$85.7M has been paid for project costs. The project team meets weekly to review cost events, and is committed to keeping project costs at \$160M.

Current Project Budget

\$132.5M	Guaranteed Maximum Price (GMP) for Construction
\$ 1.0M	Campus Utility Infrastructure Work
\$ 11.6M	Architect, Engineer, Professional Service Fees
\$ 1.0M	Campus Facilities Project Management Fee
\$.7M	Campus Remote Utility Fee and Other Project Costs
\$ 7.0M	FF&E Budget
\$ 5.0M	Graphics Budget
<u>\$ 1.2M</u>	Contingency Budget
\$160.0M	

PROJECT FUNDING PLAN UPDATE



Gift commitments of \$41.1M have been secured for new suites and loge boxes. Commitments have exceeded the \$40M fundraising goal for the project. Foundation members were provided options for payment plans up to 7 years, with \$29.2M being received towards project funding, and \$11.9M being received over the next five years towards funding debt service.

The Athletic Department funded \$5M in FY16 and \$5M in FY17. Due to the success in securing commitments for the new suites and loge boxes, and the overall solid financial position of the Athletic Department, Razorback Foundation reserves will not be used for the stadium project as originally planned.

<u>Funding Plan</u>	<u>Update</u>
\$120.0M	\$120.0M Bond Proceeds (completed Oct 2016)
	\$.8M Net Investment Earnings on Bond Proceeds
\$ 20.0M	\$ 29.2M Gift Commitments (\$41.1M total commitments)
\$ 10.0M	\$ 10.0M Athletic Funding (completed FY16-FY17)
<u>\$ 10.0M</u>	<u>\$ 0M</u> Razorback Foundation Reserves
\$160.0M	\$160.0M

SUITE/LOGE GIFT COMMITMENTS



Total Gift Commitments \$41.1M


<u>Payments</u>	<u>Project Funding</u>	<u>Debt Service Funding*</u>
FY17	\$12.1M	
FY18	\$14.4M	
FY19	\$ 2.7M	\$ 2.9M
FY20		\$ 2.8M
FY21		\$ 2.5M
FY22		\$ 1.8M
FY23		<u>\$ 1.9M</u>
	<u>\$29.2M</u>	\$11.9M

*Athletic Department will generate additional funding towards debt service from new club seating in the NEZ, and football ticket sales revenue.

ATHLETIC DEPT DEBT SERVICE



The department structured the new debt service around retirement of existing Athletic debt. Athletic revenues are currently above, and projected to remain well above, the required debt service ratios.

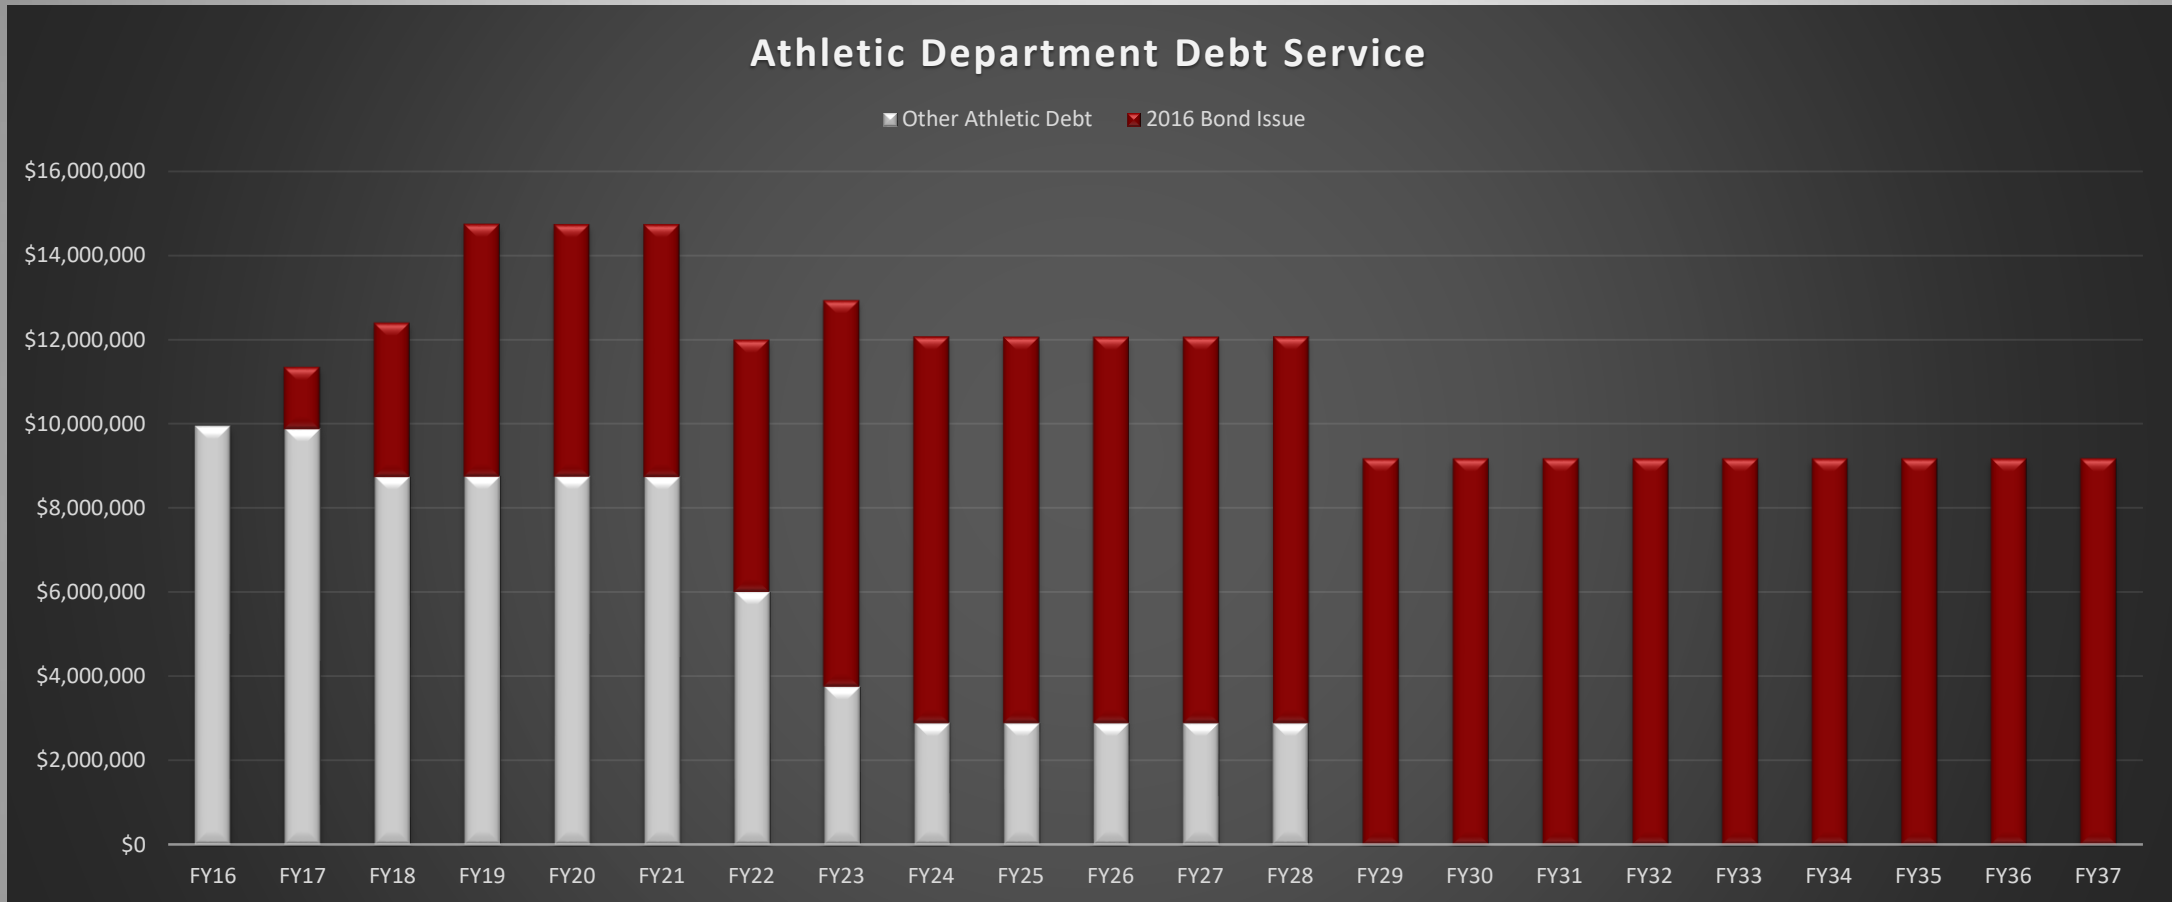

NORTH END ZONE ADDITION



Donald W. Reynolds Razorback Stadium

Fly-Through Animation Stadium Project

<http://razorbacks.ustudiopages.com/UPRfEKsCJKbr>

NORTH END ZONE ADDITION



NORTH END ZONE ADDITION

